


TSPLOST

Program Delivery – Update

March 2018



SANDY SPRINGS
GEORGIA



TSPLOST Project Status Summary To Date

- **3 Major road improvement projects are under design**
 - Johnson Ferry @ Mount Vernon roundabout project – **\$23,400,000**
 - Hammond Drive (right of way acquisition only) - **\$14,400,000**
 - Mount Vernon Corridor Analysis – Concept in progress - **\$9,900,000**
- **6 Intersection projects are under design**
 - Spalding Drive at Dalrymple Road-Trowbridge Road – **\$1,350,000**
 - Roswell Road at Grogans Ferry Road - **\$4,700,000**
 - Mount Paran at Powers Ferry Road - **\$1,800,000**
 - Riverview Road @Northside Drive - **\$2,700,000**
 - Dunwoody Club Drive @ Jett Ferry Road - **\$900,000**
 - Spalding Drive @ Pitts - **\$450,000**

Note: Budgets shown are for the total project

TSPLOST Project Status Summary To Date (Cont'd)

- **6 Sidewalk projects are under design**

- Johnson Ferry Road – Harleston Road to Glenridge Drive - **\$862,000**
- Johnson Ferry Road - Glenridge Connector to Wells Fargo - **\$114,600**
- Windsor Pkwy - Peachtree Dunwoody Road to city limit - **\$481,250**
- Northwood Drive - Kingsport to Roswell Road - **\$250,950**
- Spalding Drive - Spalding Lake Ct. to Publix – **\$1,000,000**
- Brandon Mill Road – Marsh Creek to Lost Forest Drive - **\$165,000**

Right of way acquisition is in progress

Preliminary design is in progress

Right of way acquisition is in progress

Right of way acquisition and design are complete

Coordination with Gwinnett County on project consolidation of the Spalding Drive widening project is ongoing

Concept is in progress

- **1 Trail project is under concept design**

- Ga 400 Trail project - **\$5,590,000**

Conceptual alignment is in progress


TSPLOST Project Status Summary To Date (Cont'd)

- **Last Mile Connectivity** - Steve is working on RFPs for conceptual designs/cost estimates.
 1. Peachtree Dunwoody Bike/Pedestrian Trail – Crestline Parkway to Mt Vernon Highway - \$1,551,500 (construction estimate)
 2. Abernathy Road Sidewalk – sidewalk or shared path from SR 400 to Peachtree Dunwoody Road –
 3. Ashton Woods Road – new alignment from Ashton Woods to Glenlake Parkway (possible PCID project) –
 4. Cox Trail – trail from Central Park Drive to Perimeter Center Parkway (John to contact Cox; possible PCID project) - \$513,000 (construction estimate)
 5. North Springs MARTA station bridge – bridge from Glenlake Parkway to the North Springs MARTA station
 6. Central Parkway Sidewalk Gap – short sidewalk gap on east end of Central Parkway, south side; City of Dunwoody to take the lead


T-0011 - Johnson Ferry at Mount Vernon Roundabouts

- Status:
 - Two PIOHs were held on March 8th at the B'nai Torah.
 - Three options were presented.


Roundabout Option

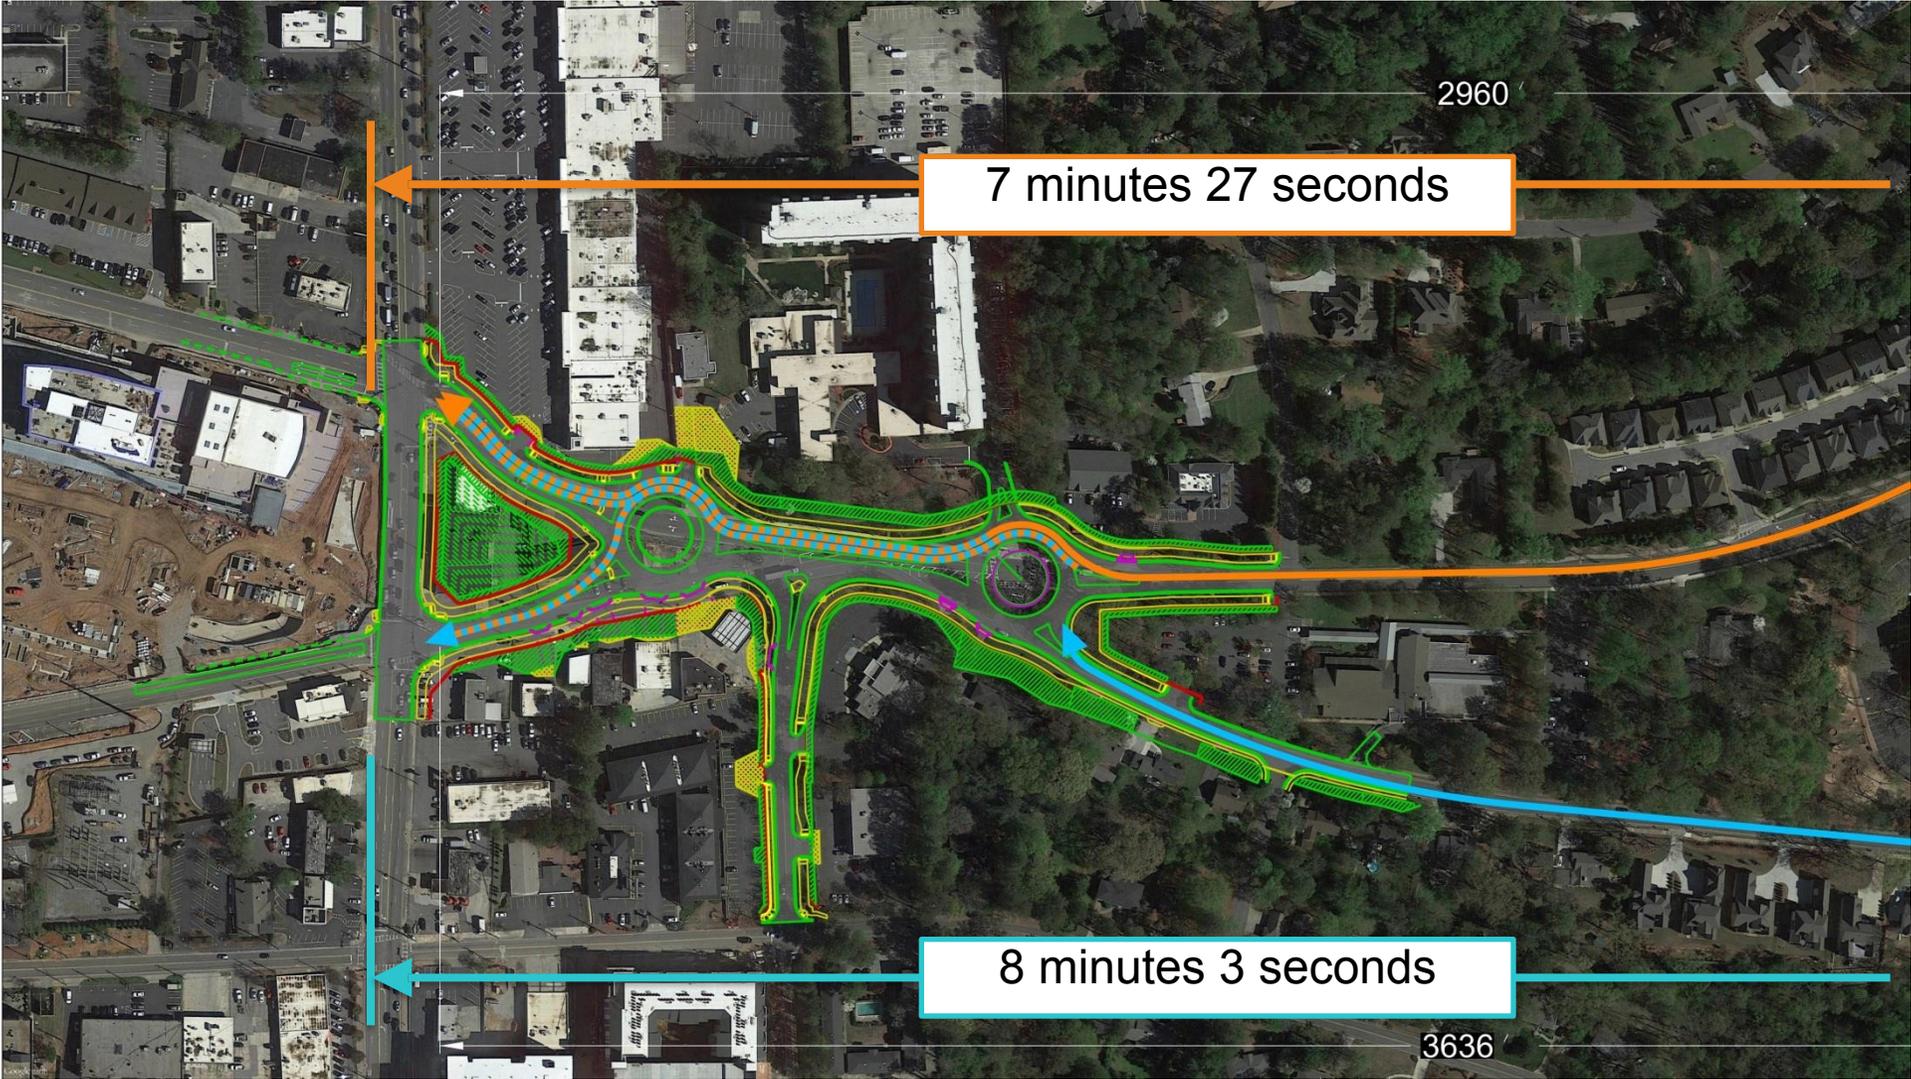

Full Grid Alternative

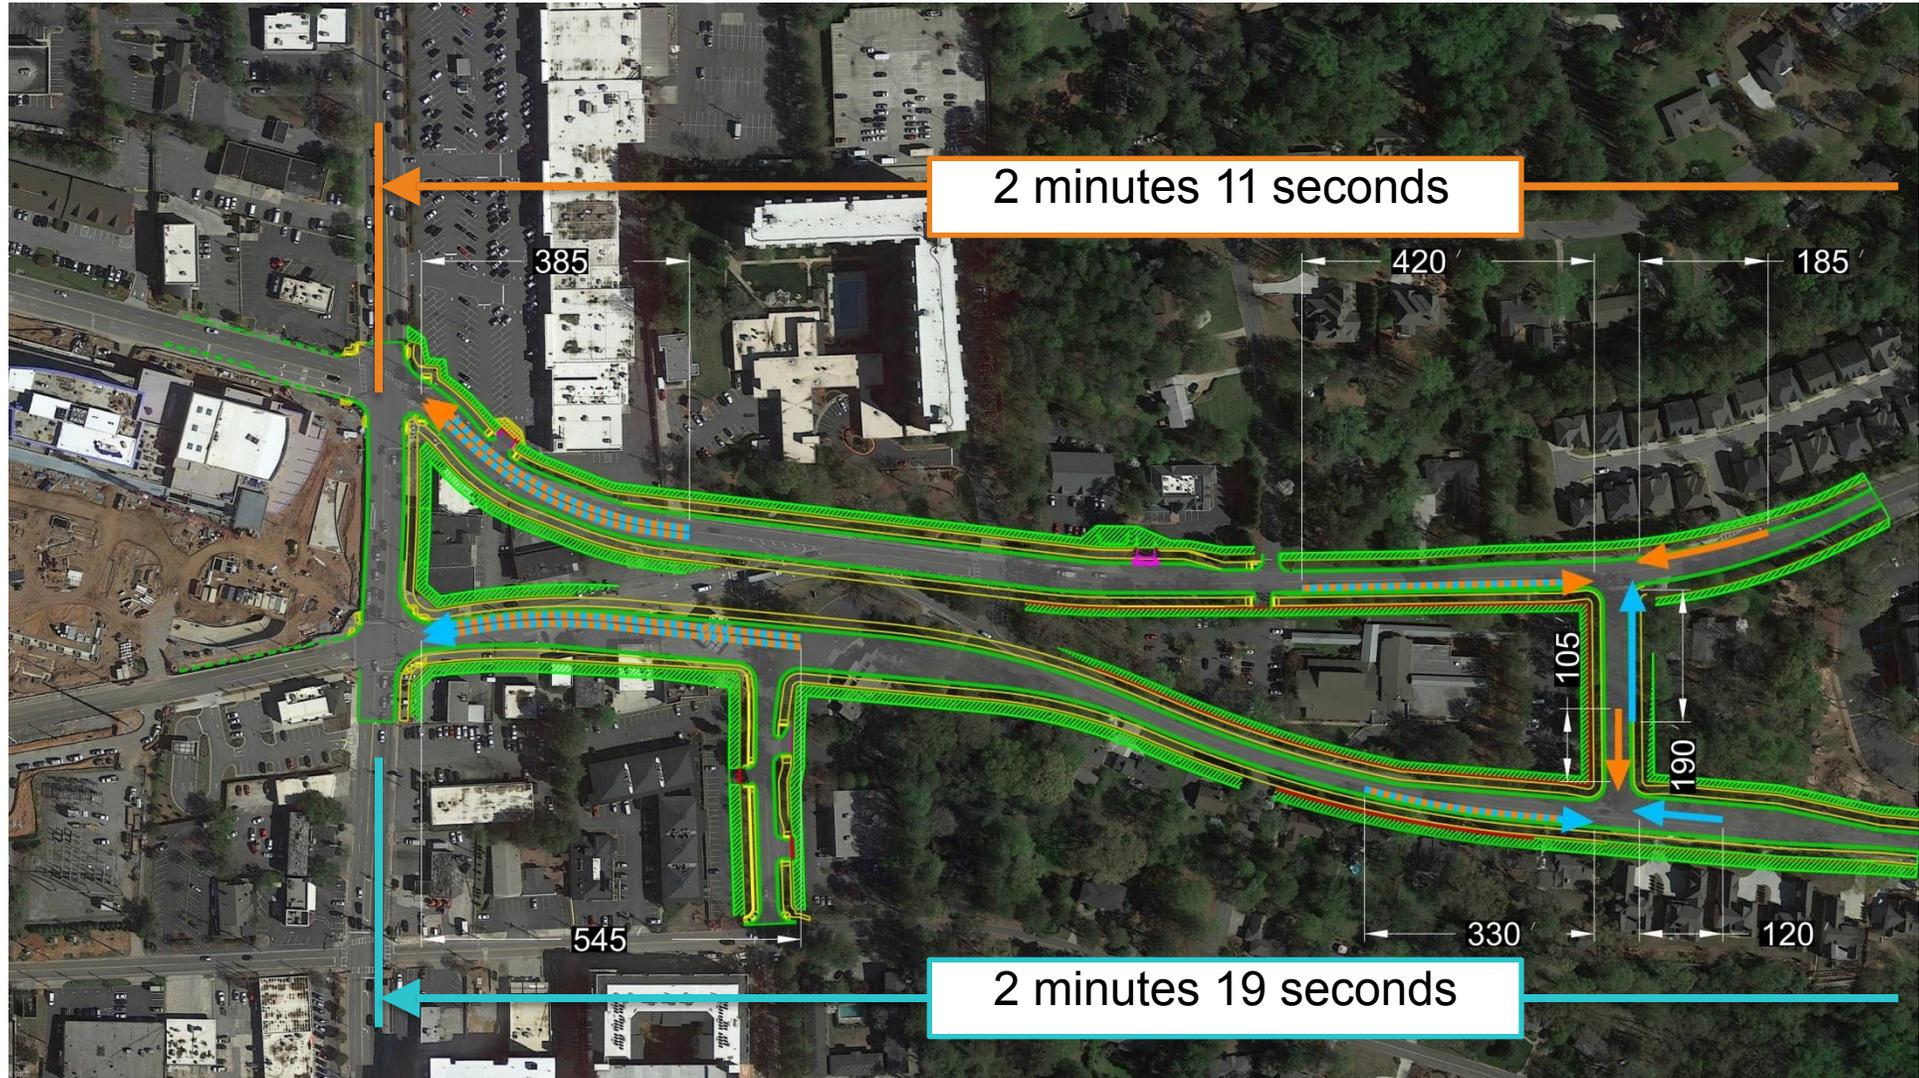

Compressed Grid

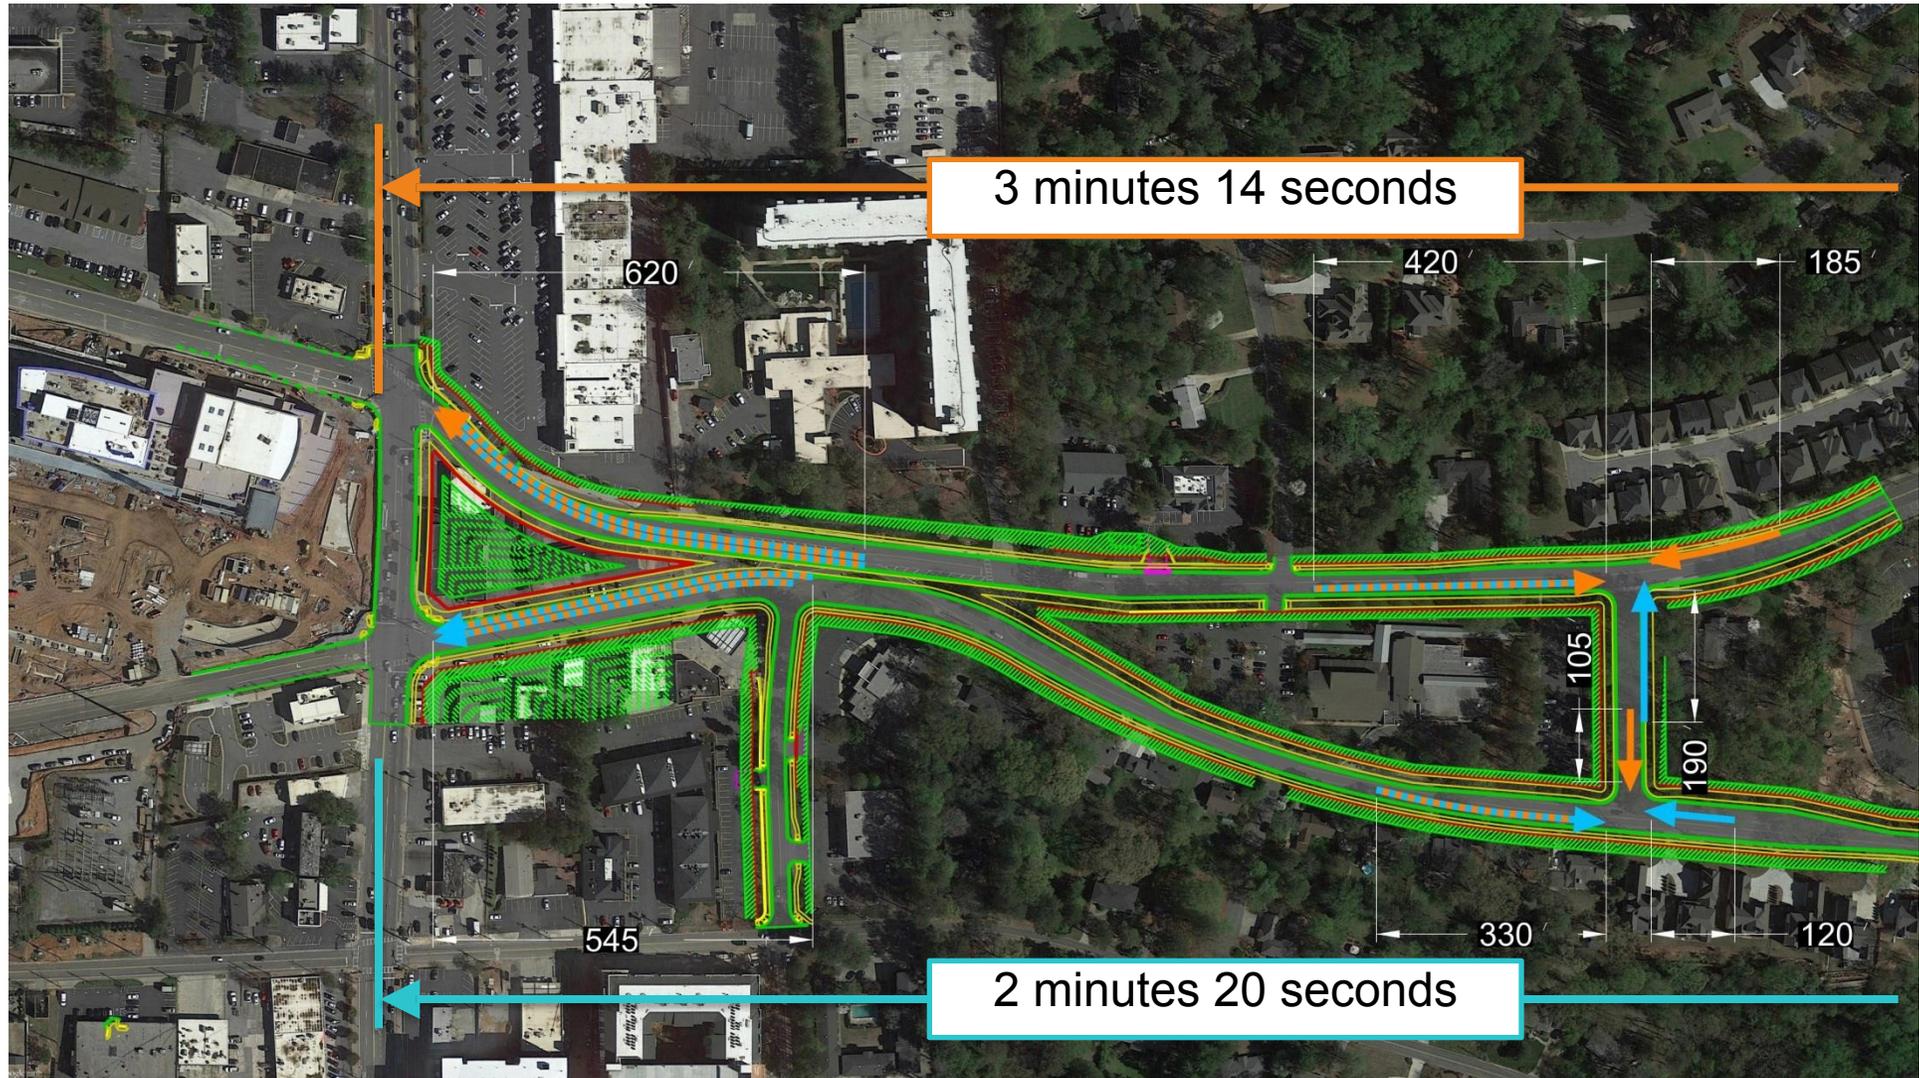

TS201 - Ga 400 Multi-use Trail - Loridans Drive to I-285

- **Status:** Preliminary Design is underway



TSPLOST Intersection Efficiency Program – Status Update

Projects Currently Under Design

Projects

Status

TS103 - Spalding @ Dalrymple-Trowbridge Int.

Right of way acquisition and final plans are in progress.

TS105 - Roswell Road @ Grogans Ferry

Preliminary plans are in progress.

TS106 - Riverview Road @ Northside Drive

Concept is to be presented to MCC for approval on March 20.

TS110 - Mt. Paran @ Powers Ferry

Final design is in progress;

TS111 - Spalding Drive @ Pitts Road

The PIOH was held on January 25th. Concept will be presented to MCC in May.

TS116 - Dunwoody Club Dr. at Jett Ferry Rd

The PIOH was held on February 8th.

TSPLOST Intersection Improvement Program Active Projects

TS103 Spalding @ Dalrymple-Trowbridge

Project provides study/concept and design drawings to correct deficiencies. Concepts for traffic signal improvements and roundabouts were analyzed. Based on feedback from the PIOH, design is proceeding with an intersection.

Status:

- KCI is working on final plans
- Right of way acquisition is in progress

Schedule:

- Anticipated construction bid in August 2018

TSPLOST Intersection Improvement Program Active Projects

TS105 Roswell Road @ Grogans Ferry Road

Project provides design drawings to install a traffic signal and implement access management along Roswell Road to correct driveway/safety deficiencies.

Status:

- A PIOH was held October 26th.
- MCC Approval granted February 6th
- Preliminary design in progress
 - Change Order being developed for Landscape Plan (GB HOA)

Current Schedule:

- Right of way to begin in May/June 2018
- Construction to begin in May 2019

TSPLOST Intersection Improvement Program Active Projects

TS110 Mount Paran @ Powers Ferry Road

Design is proceeding with a roundabout, crosswalks and ADA landings.

Schedule:

- Final design is in progress
- Right of way is scheduled to begin in March 2018
- Construction is scheduled to begin in December 2018


Status:

- ARCADIS was given direction to proceed with final design of a roundabout while taking care to preserve ROW

TSPLOST Intersection Improvement Program Active Projects

TS110 Mount Paran @ Powers Ferry Road

Installation of a roundabout, crosswalks and ADA landings.

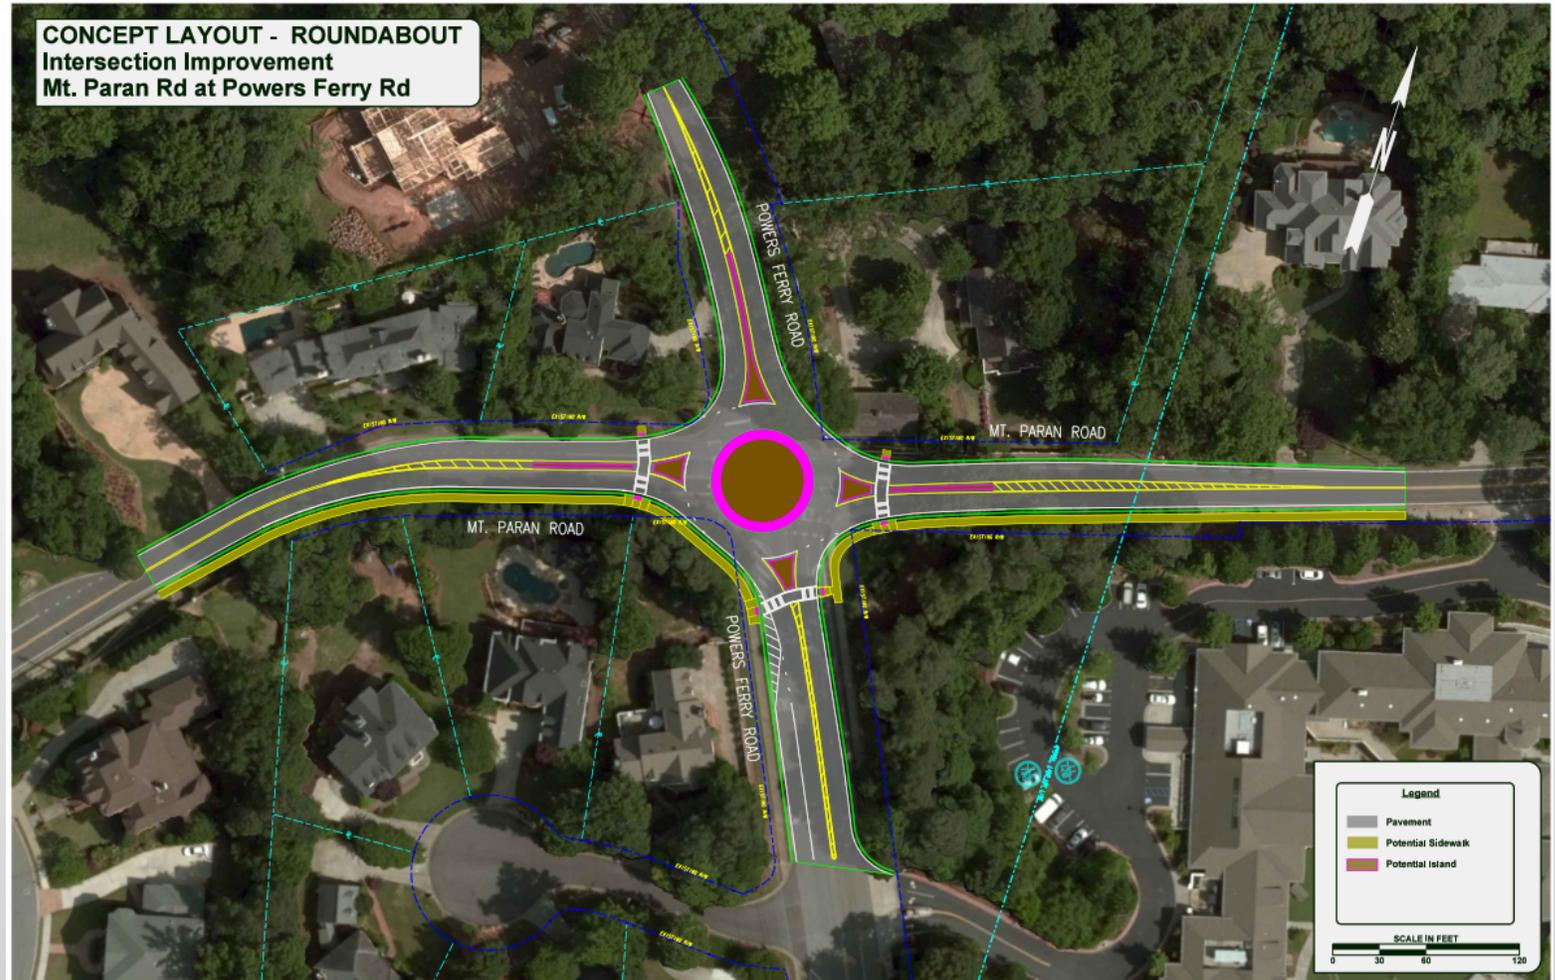

TSPLOST Intersection Improvement Program Active Projects

TS116 Dunwoody Club Dr. at Jett Ferry Rd.

Project scope will provide concept/design for the intersection including a roundabout (likely – to be finalized by March 12th) or traffic signal.

Schedule:

- PIOH was held Feb. 8th

Status:

- Flashing Stop Signs to be studied by CALYX

TSPLOST Intersection Improvement Program Active Projects

TS116 Dunwoody Club Dr. at Jett Ferry Rd.



TSPLOST Intersection Improvement Program Active Projects

TS106 Northside Dr. @ Riverview-Old Powers Ferry

An intersection improvement at the intersection of Northside Dr. at Old Powers Ferry-Riverview Dr. is planned.

Schedule:

- Feb 1st PIOH held
- Tentative Let Winter '18/'19

Status:

- Geotech Survey to be completed week of March 5th

TSPLOST Intersection Improvement Program Active Projects

TS106 Northside Dr. @ Riverview-Old Powers Ferry



TSPLOST Intersection Improvement Program Active Projects

TS111 Spalding Rd. @ Pitts Rd.


Additional turn lanes and an upgraded traffic signal at the intersection of Northside Dr. at Old Powers Ferry-Riverview Dr. is planned.

Schedule:

- Working on Change Order for items needed before presenting to Council
- Concept presented at Jan 25th PIOH

TSPLOST Intersection Improvement Program Active Projects

TS111 Spalding Rd. @ Pitts Rd.

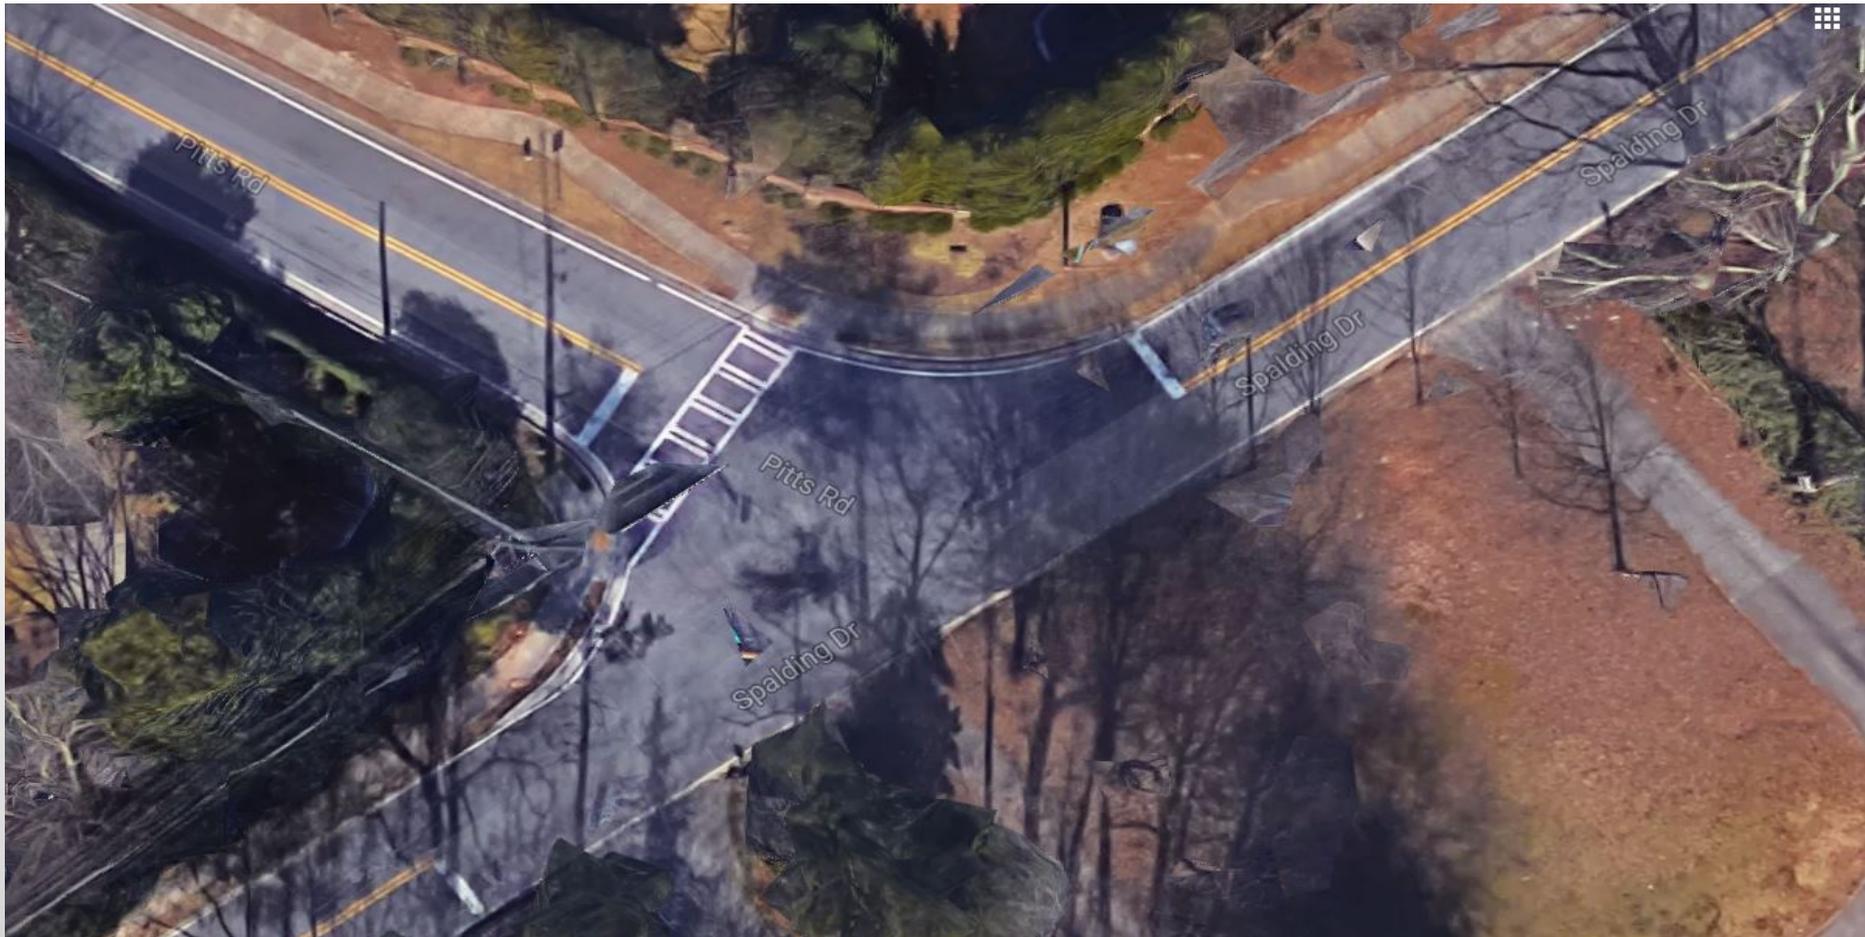

TSPLOST Sidewalk Projects – Status Update

Projects Currently Under Design

Projects

TS162 Johnson Ferry – Harleston Road to Glenridge Drive

TS163 Johnson Ferry – Glenridge Connector to Wells Fargo

TS164 Windsor Parkway – Peachtree Dunwoody Road to city limit

TS165 Northwood Drive – Kingsport to Roswell Road

TS166 Spalding Drive – Spalding Lake Court to Publix

TS167 Brandon Mill Road – Marsh Creek to Lost Forest Drive

Status

Preliminary design in progress.

Preliminary design in progress.


Preliminary design in progress.

Final design in progress.

Concept is on hold; coordination with Gwinnett County and Peachtree Corners is ongoing regarding the widening of Spalding Drive.

Concept design is in progress.

Concept Exhibit
 Project TS163
 Johnson Ferry Road (800 Johnson Ferry Rd to LDP16-00038)
 Sidepath Project

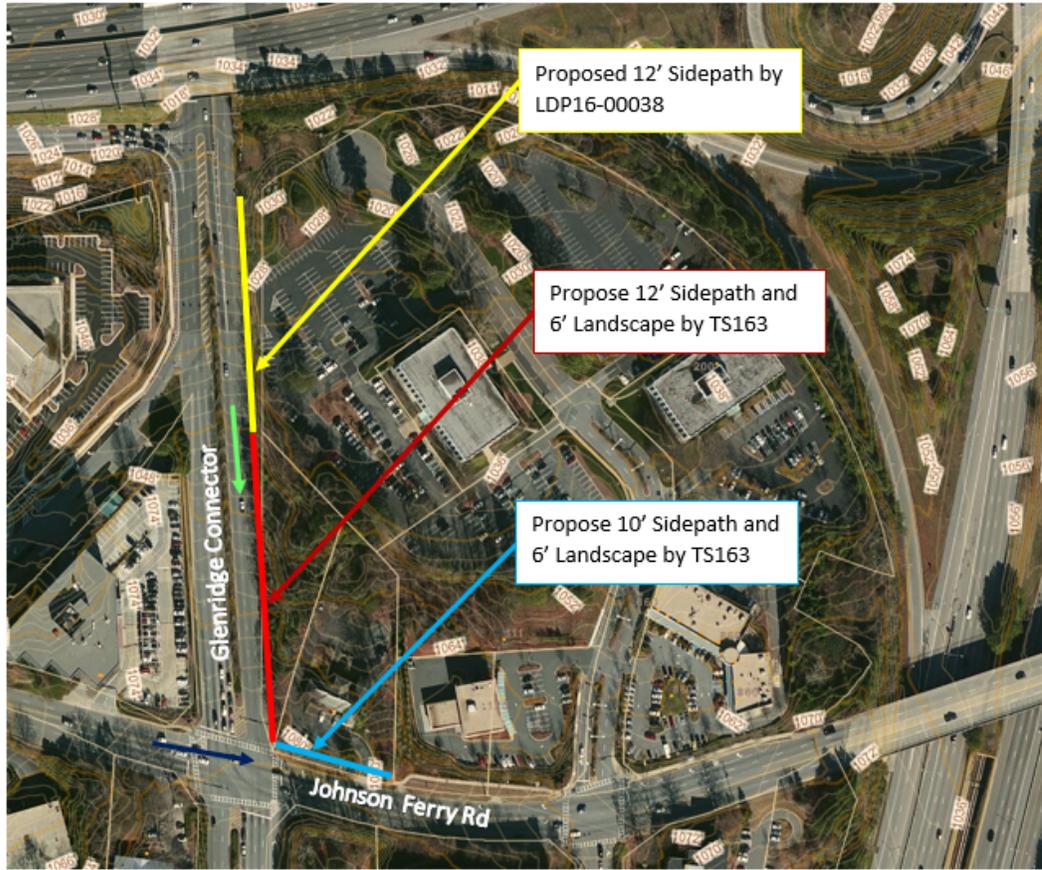


Project TS163


Johnson Ferry at Glenridge Connector

Status:

- Completes nearby PCID streetscape to intersection and pedestrian crossings/enhances pedestrian access to transit
- Increased scope to extend Sidepath to the proposed Sidepath by development on Glenridge Connector
- Concept design is in progress; project is on schedule

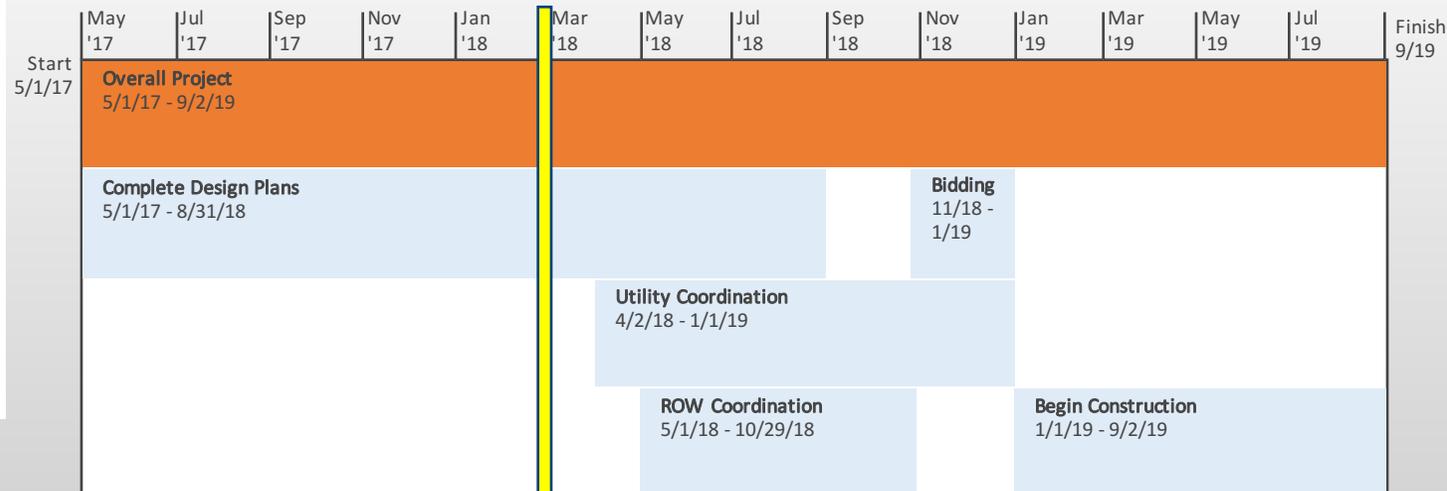

Concept Exhibit
Windsor Parkway (Crestwicke Pointe to City Limit)
Sidewalk Project

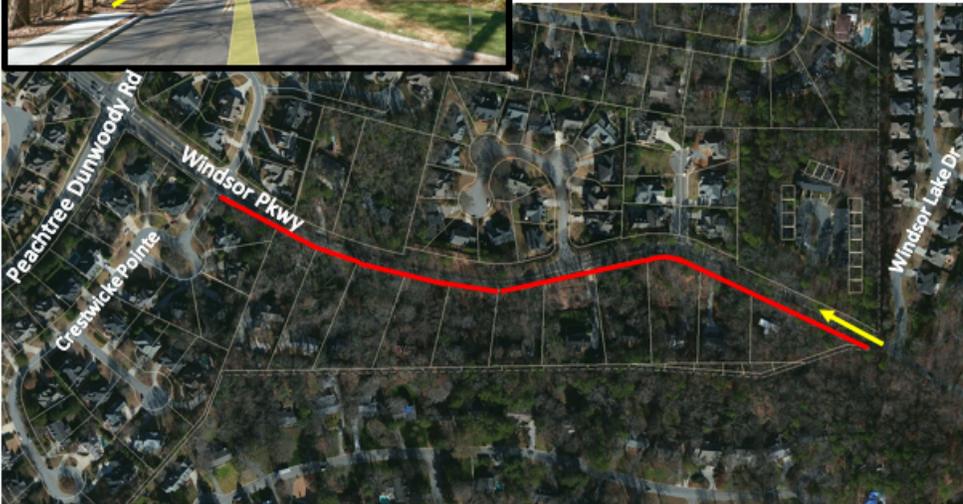


Project TS164

Windsor Parkway - Crestwick Pointe to City Limit

Status:

- Extends sidewalk network on Windsor Parkway to City Limit improving connectivity to Windsor pedestrian bridge
- Preliminary design is in progress; project is on schedule

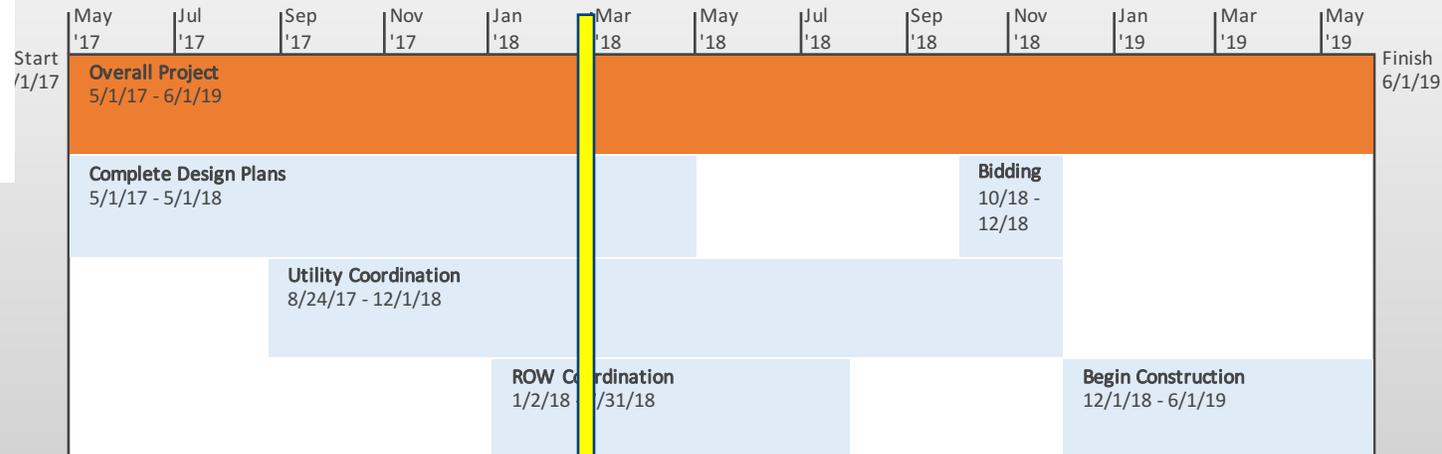

Concept Exhibit
Northwood Drive (Kingsport Dr to Roswell Rd)
Sidewalk Project




Project TS165

Northwood Drive – Kingsport Dr. to Roswell Road

Status:

- Ties to recent streetscape improvements at Roswell Road and future CDBG Streetscape improvements
- Design is completed; project is on schedule

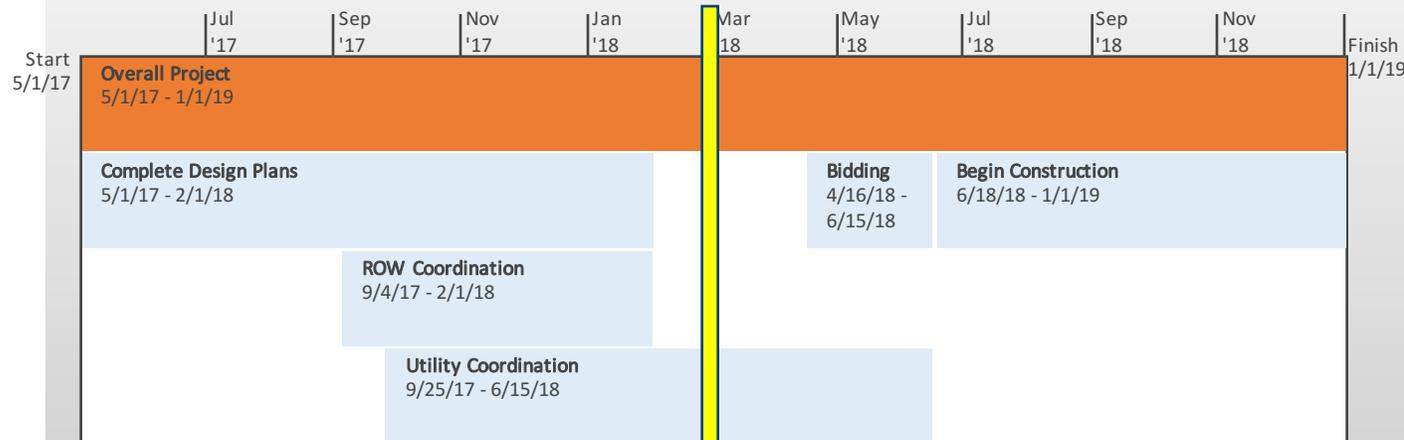

Concept Exhibit
 Spalding Drive (Spalding Lake Ct to River Exchange Dr)
 Sidewalk Project




Project TS166

Spalding Drive – Spalding Lake Court to River Exchange


Status:

- Extends sidewalk network from commercial River Exchange to residential neighborhoods
- Includes bicycle/pedestrian bridge
- Project currently on HOLD; coordination with Gwinnett County ongoing.

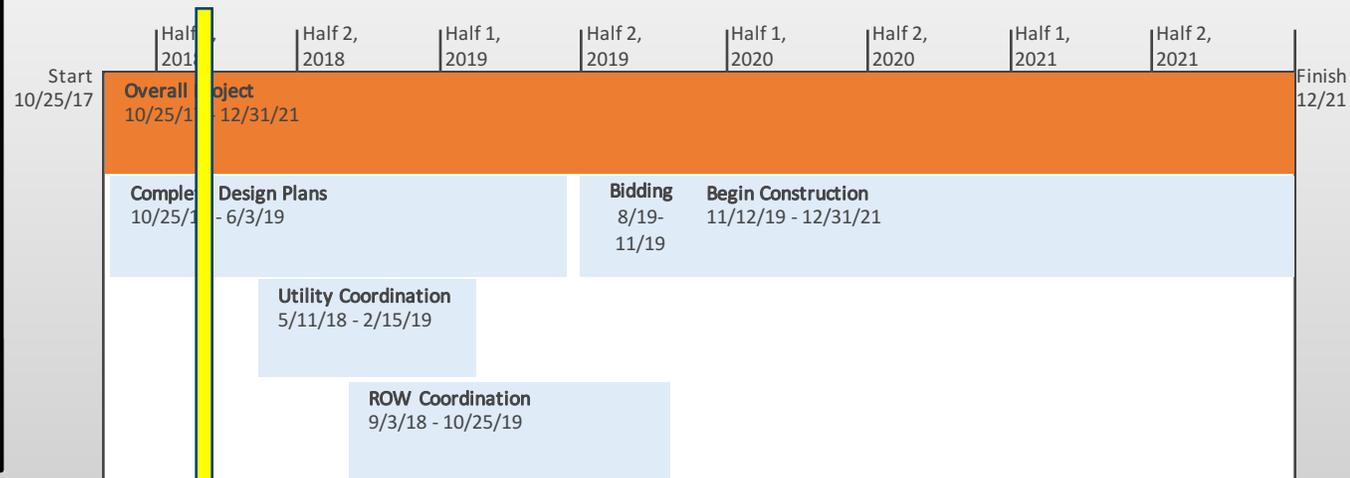

Concept Exhibit
Project TS-167

Brandon Mill Road (Marsh Creek to Lost Forest Drive)
Sidewalk Project (TSPLOST)

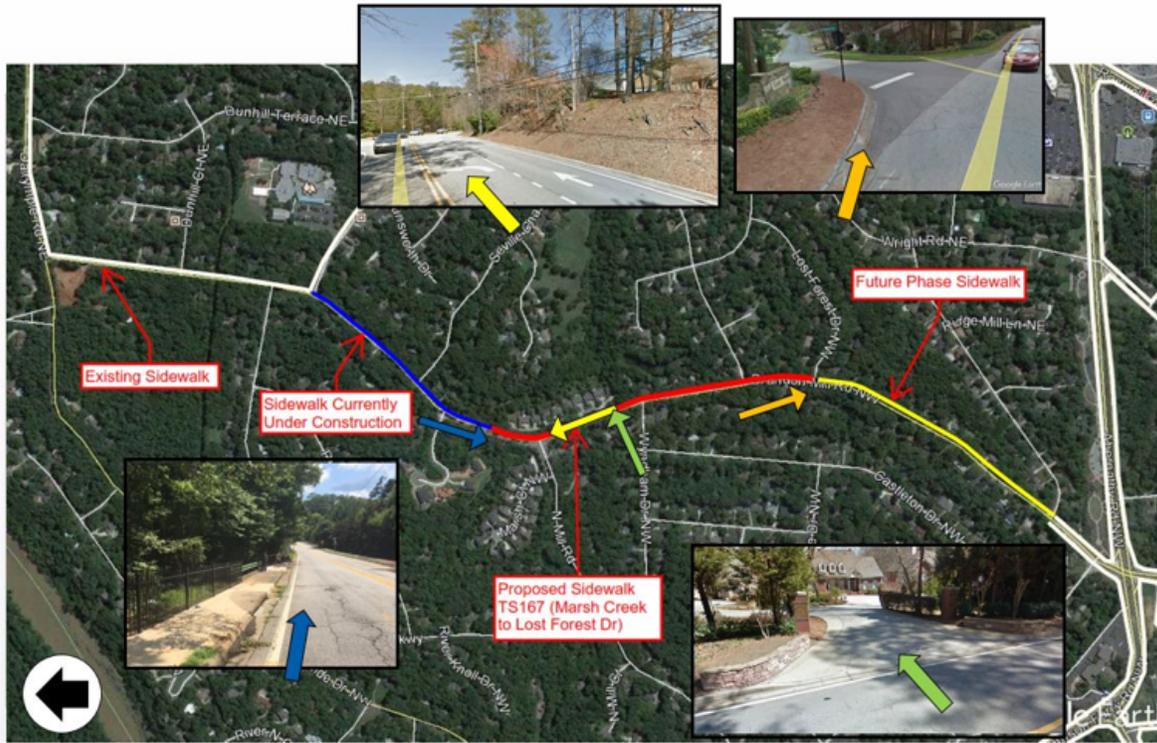

Project TS167

Brandon Mill Road – Marsh Creek to Lost Forest Drive

Status:

- Extends sidewalk network from Marsh Creek to Lost Forest Drive
- Concept design is in progress; project is on schedule.

